BEYOND LIMITS

Serbian Pavilion - Proposed Planning
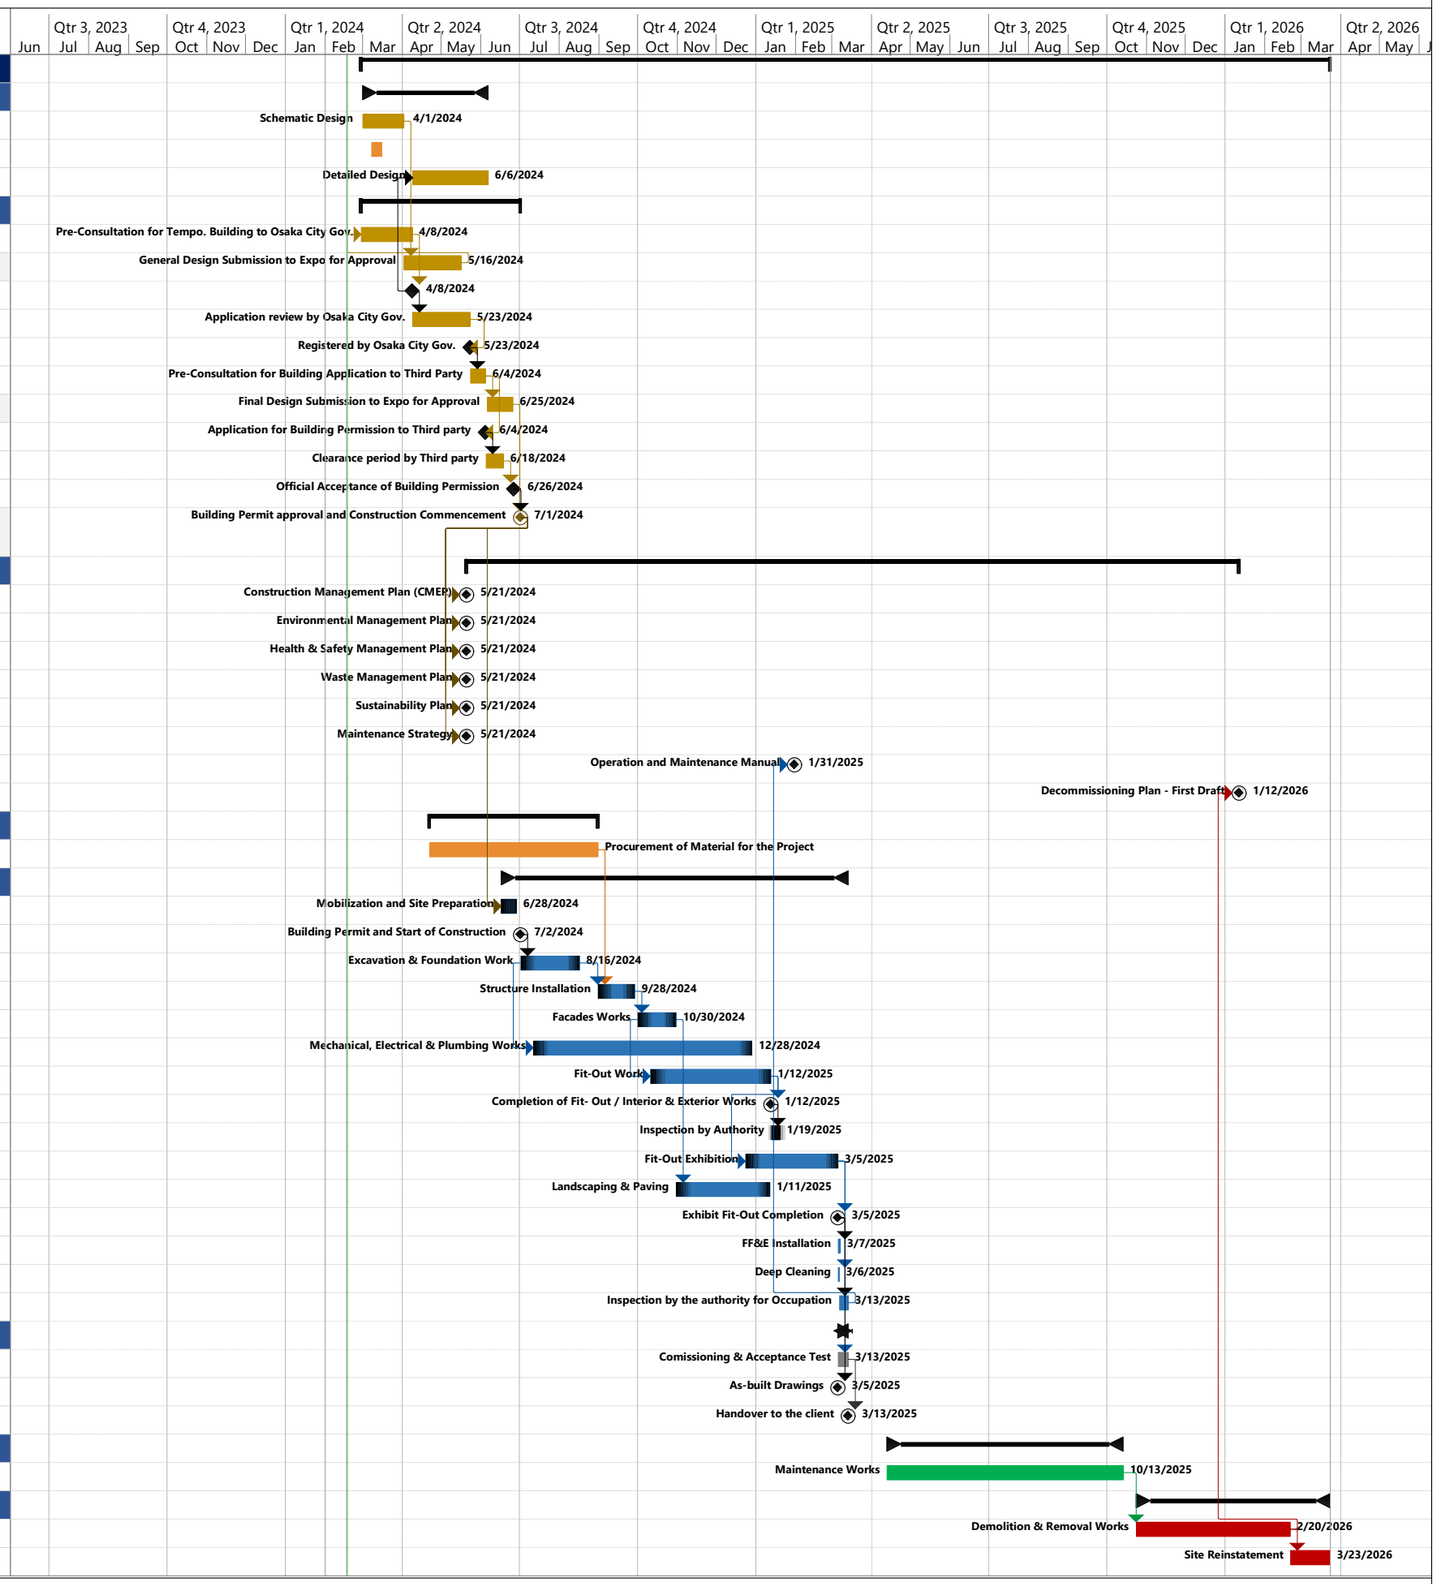
ID	ID	WBS	Task Name	Duration	Start
1	1	SERBIA-EX25-01	Serbian Pavilion - World Expo Osaka 2025	528 days	February 29, 2024
2	2	SERBIA-EX25-01.1	DESIGN PHASE	66 days	March 1, 2024
3	3	SERBIA-EX25-01.1.1	Schematic Design	21 days	March 1, 2024
4	4	SERBIA-EX25-01.1.2	Geotechnical test - Soil Survey	6 days	March 8, 2024
5	5	SERBIA-EX25-01.1.3	Detailed Design	40 days	April 9, 2024
6	6	SERBIA-EX25-01.2	Building Administration to the Authorities	84 days	February 29, 2024
7	7	SERBIA-EX25-01.2.1	Pre-Consultation for Tempo. Building to Osaka City (	27 days	February 29, 2024
8	8	SERBIA-EX25-01.2.2	General Design Submission to Expo for Approval	30 days	April 2, 2024
9	9	SERBIA-EX25-01.2.3	Application for Tempo Building Application	0 days	April 8, 2024
10	10	SERBIA-EX25-01.2.4	Application review by Osaka City Gov.	1.5 mons	April 9, 2024
11	11	SERBIA-EX25-01.2.5	Registered by Osaka City Gov.	0 days	May 23, 2024
12	12	SERBIA-EX25-01.2.6	Pre-Consultation for Building Application to Third Pa	8 days	May 24, 2024
13	13	SERBIA-EX25-01.2.7	Final Design Submission to Expo for Approval	14 days	June 6, 2024
14	14	SERBIA-EX25-01.2.8	Application for Building Permission to Third party	0 days	June 4, 2024
15	15	SERBIA-EX25-01.2.9	Clearance period by Third party	10 days	June 5, 2024
16	16	SERBIA-EX25-01.2.10	Official Acceptance of Building Permission	0 days	June 26, 2024
17	17	SERBIA-EX25-01.2.11	Building Permit approval and Construction Commencement	0 days	July 1, 2024
18	18	SERBIA-EX25-01.3	Plans & Documentation Submittals for Approval	423 days	May 21, 2024
19	19	SERBIA-EX25-01.3.1	Construction Management Plan (CMEP)	0 days	May 21, 2024
20	20	SERBIA-EX25-01.3.2	Environmental Management Plan	0 days	May 21, 2024
21	21	SERBIA-EX25-01.3.3	Health & Safety Management Plan	0 days	May 21, 2024
22	22	SERBIA-EX25-01.3.4	Waste Management Plan	0 days	May 21, 2024
23	23	SERBIA-EX25-01.3.5	Sustainability Plan	0 days	May 21, 2024
24	24	SERBIA-EX25-01.3.6	Maintenance Strategy	0 days	May 21, 2024
25	25	SERBIA-EX25-01.3.7	Operation and Maintenance Manual	0 days	January 31, 2025
26	26	SERBIA-EX25-01.3.8	Decommissioning Plan - First Draft	0 days	January 12, 2026
27	27	SERBIA-EX25-01.4	Building Material Procurement	90 days	April 22, 2024
28	28	SERBIA-EX25-01.4.1	Procurement of Material for the Project	90 days	April 22, 2024
29	29	SERBIA-EX25-01.5	BUILDING PHASE	260 days	June 17, 2024
30	30	SERBIA-EX25-01.5.1	Mobilization and Site Preparation	12 days	June 17, 2024
31	31	SERBIA-EX25-01.5.2	Building Permit and Start of Construction	0 days	July 2, 2024
32	32	SERBIA-EX25-01.5.3	Excavation & Foundation Work	43 days	July 2, 2024
33	33	SERBIA-EX25-01.5.4	Structure Installation	26 days	August 31, 2024
34	34	SERBIA-EX25-01.5.5	Facades Works	29 days	October 1, 2024
35	35	SERBIA-EX25-01.5.6	Mechanical, Electrical & Plumbing Works	160 days	July 12, 2024
36	36	SERBIA-EX25-01.5.7	Fit-Out Work	90 days	October 11, 2024
37	37	SERBIA-EX25-01.5.8	Completion of Fit- Out / Interior & Exterior Works	0 days	January 12, 2025
38	38	SERBIA-EX25-01.5.9	Inspection by Authority	7 days	January 13, 2025
39	39	SERBIA-EX25-01.5.10	Fit-Out Exhibition	72 days	December 24, 2024
40	40	SERBIA-EX25-01.5.11	Landscaping & Paving	70 days	October 31, 2024
41	41	SERBIA-EX25-01.5.12	Exhibit Fit-Out Completion	0 days	March 5, 2025
42	42	SERBIA-EX25-01.5.13	FF&E Installation	2 days	March 6, 2025
43	43	SERBIA-EX25-01.5.14	Deep Cleaning	1 day	March 6, 2025
44	44	SERBIA-EX25-01.5.15	Inspection by the authority for Occupation	7 days	March 7, 2025
45	45	SERBIA-EX25-01.6	TESTING AND PAVILION DELIVERY	8 days	March 5, 2025
46	46	SERBIA-EX25-01.6.1	Comissioning & Acceptance Test	8 days	March 6, 2025
47	47	SERBIA-EX25-01.6.2	As-built Drawings	0 days	March 5, 2025
48	48	SERBIA-EX25-01.6.3	Handover to the client	0 days	March 13, 2025
49	49	SERBIA-EX25-01.7	MAINTENANCE PHASE	184 days	April 13, 2025
50	50	SERBIA-EX25-01.7.1	Maintenance Works	184 days	April 13, 2025
51	51	SERBIA-EX25-01.8	DISMANTLING PHASE	151 days	October 24, 2025
52	52	SERBIA-EX25-01.8.1	Demolition & Removal Works	120 days	October 24, 2025
53	53	SERBIA-EX25-01.8.2	Site Reinstatement	31 days	February 21, 2026
